DailyDutch

Free daily Dutch lessons — from project charter to (almost) done

Project Management · SRH Haarlem University of Applied Sciences
[Team names] · [Presentation date]

Agenda

1. **Initiation**
   Problem, business case, project charter

2. **Planning**
   Scope, stakeholders, WBS, schedule, risks

3. **Execution**
   What we built and how

4. **Monitoring & control**
   Quality, results, Definition of Done

5. **Closure**
   Lessons learned, deployment, next steps

Learning Dutch should not cost money or patience

The problem

- Most apps need subscriptions or accounts
- Sentences use words the learner never saw
- Words are learned once, then forgotten
- No clear daily rhythm

Our solution: DailyDutch

- Free, no login, no ads
- Only words already taught — checked by a script
- Spaced-repetition review built in
- One 10–15 min lesson per day, 120 days

Project charter: five SMART objectives

01

Complete A1–A2 curriculum

Target: 120 lessons

Met

02

Only already-taught words

Target: 0 validator errors

Met

03

Long-term retention

Target: Spaced-repetition review

Met

04

Phone + offline

Target: Installable PWA

Met

05

Public and free

Target: Live on Vercel

Open

Budget €0 · Constraint: no backend, all progress stays in the learner's browser · Sponsor: course lecturer

Scope: what we build — and what we don't

In scope

- 120 lessons: words, grammar, dialogue
- Lesson flow + exercises
- Spaced-repetition review
- My words, home dashboard, streak
- Pronunciation page + listen buttons
- PWA: install on phone, offline
- Content tooling, tests, deployment

Out of scope

- Accounts / sync
- Payments, ads
- Native apps
- B1 and higher
- Human audio
- Teacher dashboards

Stakeholders: power × interest

Power ↑

Keep satisfied

Hosting provider (Vercel)
Stay within free tier

Manage closely

Lecturer / examiner (sponsor)
Status updates, sign-off

Monitor


Open-data providers
CC BY-SA attribution

Keep informed

Learners, classmates, test users
Live link, feedback

Interest →

Work breakdown structure

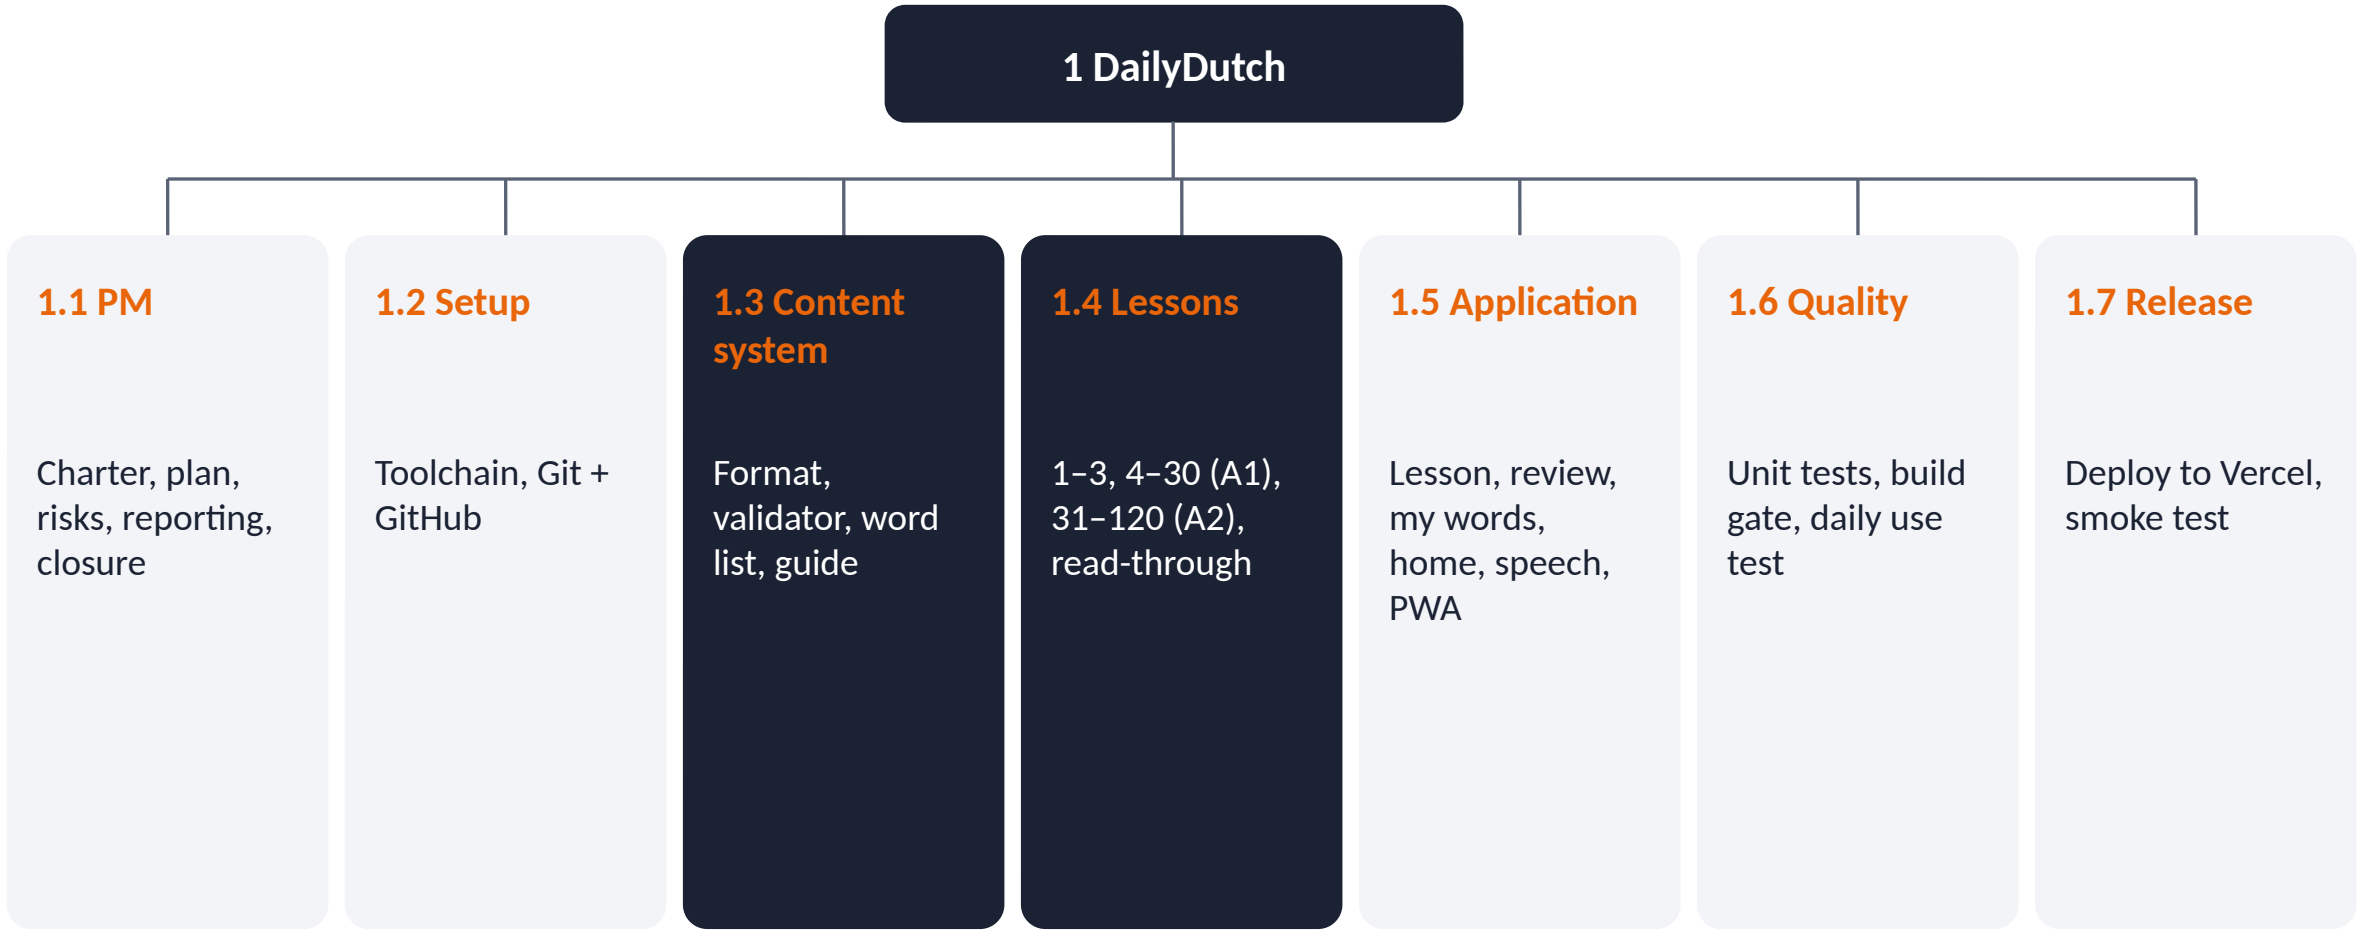

Full WBS tree: project-management/02-project-plan.md

Schedule: milestones planned vs. reached



● reached ○ remaining

Risk management: top risks and responses

Risk	P×I	Response	Status
R1 Dutch errors in lessons 4–120	**16**	Read-through by Dutch speaker	**Open**
R4 Not finished before deadline	**15**	MVP first, tooling for speed	**Mostly closed**
R3 Scope creep (accounts, sync…)	**12**	Out-of-scope list, MoSCoW	**Controlled**
R2 Sentence uses untaught word	**9**	Validator in build	**Closed**
R6 Learner loses browser progress	**9**	Accepted, explained	**Accepted**
R7 Deployment / hosting fails	**8**	Static build, any host works	**Open**

Scale 1–5 for probability (P) and impact (I). Full register with 10 risks: 03-risk-register.md

What we built

1 Daily lesson

Words → grammar → dialogue, with gap-fill exercises

2 Review

Spaced repetition: 8 boxes, 1 to 60-day gaps

3 Home

Today's lesson, words due, streak, words known

4 My words

Add your own words to the review

5 Listen + Sounds

Dutch speech voice; pronunciation rules page

6 Works offline

Install on phone (PWA), no login, no backend

How we built 120 lessons fast and safely

1

Open data

Frequency list + Wiktionary → word list with articles, plurals, verb forms

→

2

Coverage

Script picks the most frequent words not yet taught

→

3

Write

Authoring guide + 3 reference lessons set tone and format

→

4

Validate

Build fails if any sentence uses an untaught word

Tech: Vite + React + TypeScript · Vitest · static site · data CC BY-SA 4.0

Results in numbers

120
lessons (A1–A2)

1,822
words taught

660
grammar exercises

1,436
dialogue lines

0
validator errors

€0
total cost

Quality control: automated gates + human review

Check	Tool	Result
Known-words-only rule	`npm run check`	**120 lessons OK**
Unit tests (SRS, dates, answers)	`npm test (Vitest)`	**7 / 7 pass**
Type safety	`tsc --noEmit`	**Pass**
Build gate	`npm run build`	**Pass**
Language + story review	`Human read-through`	**Pending**
Real-life use	`Daily use test`	**Pending**

Definition of Done: 7 of 13 criteria met



Done

- ✓ 120 lessons with words, grammar, dialogue
- ✓ Validator: 0 errors
- ✓ Unit tests pass
- ✓ Type-check + build pass
- ✓ All pages work
- ✓ PWA installable + offline
- ✓ Code in Git + GitHub

Remaining

- ☐ Read-through lessons 4–120
- ☐ Daily use test + fixes
- ☐ Deployed on Vercel
- ☐ Live smoke test (desktop + phone)
- ☐ PLAN.md updated
- ☐ Documents + sponsor sign-off

Lessons learned

Keep doing

- Build a thin MVP first, then scale
- Automate the rule that matters most
- Reuse open data before writing by hand
- Document the process (authoring guide)
- Write down what is out of scope

Do better next time

- Deploy early and continuously
- Plan review time per batch of content
- Baseline planned dates at kickoff
- Get test users in week 1
- Write charter + risks before coding

Next steps to close the project

1	**Review**	Read-through lessons 4–120, fix Dutch + story	[Owner] · [date]
2	**Test**	Daily use test, fix annoyances	[Owner] · [date]
3	**Deploy**	Vercel: Vite preset, npm run build → dist	[Owner] · [date]
4	**Close**	Live smoke test, update PLAN.md, sponsor sign-off	[Owner] · [date]

Dank je wel!

Questions? · Live demo: [live URL after deployment]
